



CARE Knowledge Base

Knowledge Engine for CARE, by CARE!

Search by Category

All categories

▼

Search

Enter a search term, select a category and click **Search** or select an icon below.

[All Articles](#) [G2](#) [G3](#) [Car Park RMS](#) [RevPlan](#) [SmartSpace](#) [Casper](#) [Optix](#) [Assets](#)

Agent to Agent Migration

Document Control

Document Information			
Name of Document	Process Document_Agent to Agent_1.00	-	-
Version Number	1.00	-	-
Prepared By	Sr. Process Analyst	Name	Sneha Nirgude
Reviewed By	Migration Project Lead	Name	Nihar Joshi
Approved By	Process Team Lead	Name	Karl Lobo

Categories

Select Category

Recent Posts

- [HLTN/hiltonEnableSmallGroupProductsAndInventoryLimitForNewPropertyStep](#)
- [Service Recovery Procedure – IDeaSOperaAgent Service in “Stopping” State](#)
- [Processing Failures Due to Data Type Mismatch for MGM Resorts](#)
- [Dynamic Optimization](#)
- [HLTN/Handling Error for SAS Dataset Encoding Job](#)

1 Introduction

1.1 Purpose

The purpose of this document is to prepare a standard process for Agent-to-Agent migrations to ensure the timely migration of the projects and identify the different tasks performed in the migration. This document will give a clear picture of the different steps and tasks performed in the Agent-to-Agent migration.

1.2 Scope

This document will help in identifying the different steps involved in the migration of properties from Agent to Agent, and the different teams involved in the process of migration.

1.3 Intended Audience

The target audience for this document is the team and the stakeholders involved in Agent-to-Agent migration projects.

E.g. – Project Manager, Project Lead, Team Members etc.

1.4 Abbreviation

Abbreviation	Description
ICS	Installation, Configuration & Support
ROA	<u>Revenue Optimization</u> Analyst
SPM	Systems Performance Monitoring
CPM	Client Project Manager
PID	Property Inbound Data
SOW	Scope of Work
RT	<u>Room Type</u>
MS	Market Segment
PMS	Property Management System
FVR	<u>Forecast Validation</u> Report
AMS	Analytical Market Segment
CCFG	Create & Commit <u>Forecast Group</u>
RSS	<u>Rate Shopping</u> System
CMA	Configuration Management Access
BDE/DE	Business Day End/Day End

2 Assumptions

Estimation is based on Estimation History document.

3 Phases

This section will give the breakdown of tasks in a phase wise manner.

Recent Comments

Pranav Thakar on [Hilton/Processing Failure – non positive offset value for Product](#)

Ranjit on [Hilton/Processing Failure – non positive offset value for Product](#)

Ranjit on [Service Recovery Procedure – IDeaSOperaAgent Service in “Stopping” State](#)

Ranjit on [Processing Failures Due to Data Type Mismatch for MGM Resorts](#)

Ranjit on [Accor Client Handling Process Guide](#)

Phases	Tasks
1	Task 1 to Task 8
2	Task 9 to Task 19
3	Task 20 to Task 25

4 Entry Criteria

- Project is at Initiation & Execution Stage

5 Pre-Requisites & Assumptions

- It is assumed that the project team has the access to the following tools & has the required knowledge to use the tools and execute the project
- G3 CMA
- G3 RMS

6 Activities Performed

Task 1 – Send & Discuss PID with the client

- In this step Case Owner will send out the PID Primary Inbound Data Switch Questionnaire and discuss the content with the client.
- The Case Owner will also familiarize themselves with supporting migration content that is available in the PMS Migration Guide

Task 2 – Attach PID form & SOW on case level

- In this step the Case Owner will attach the filled PID form and SOW to the related case.
- Once this task is done the Case Owner will update the task with relevant comments and update the task status as completed

Task 3- Attach Opera Agent Questionnaire to the case

- In this step the Case Owner will attach the filled Opera Agent Questionnaire to the related case.
- Once this task is done the Case Owner will update the task with relevant comments and update the task status as completed

Task 4- Migration Date Information

- Case owner will enter the migration date into the case description along with the following details
- Cut over date
- Name and version of the new PMS
- Details of any changes in configuration moving from the old PMS to the New PMS
- Once this task is done the Case Owner will update the task with relevant comments and update the task status as completed.

Task 5.1 – Migration Changes

- In this task the case owner will confirm the following changes
- Group Code/Group ID
- Reservation ID
- Confirmation No.
- Rate Codes
- Market Segment
- Room Types
- Property/Resort Code
- The above information (With Change or Without Change) is shared with the respective project migration team.
- Once this task is done the Case Owner will update the task with relevant comments and update the task status as completed.

Note – This is very important information that decides if a particular migration activity is with or without AMS recoding.

Task 5.2 – Provide Migration Sheet to the Case Owner

- In this step the case owner will discuss the migration sheet with the client & provide the necessary mapping.
- This sheet is then shared across with the respective project migration team.

Note- This sheet will be provided if there are any migration changes. If there are no changes then the Case Owner will inform the same to the respective project migration team.

Task 6 – Migration Changes_Pre Data Collection

- In this step the team will take the back up of pre-data
- For the same follow the Task 1 activities mentioned in [Process Document_Pre-Post Forecast & Decision Verification_1.00](#)

Task 6.1 – Active Block/In-House and Future Reservations Check

- Before starting this task check the status of the CMA application.
- So here the ICS team will go to the [G3 CMA](#), run a query 'Group Mapping for PMS Migration' and take the dump of the group codes that is present in the existing G3 system. This excel sheet will be given an appropriate name and saved on the required path


**CONFIGURATION
MANAGER**

SQL Reports Admin Parameters File Explorer

Run SQL Adhoc SQL View Scheduled SQL Edit Scheduled SQL

Run SQL

Selected Query: **Group Mapping for PMS migration**

SFDC Case: Get

☒ Select One or More Chains
☐ Import Property Codes

Prod Instances:

PROD_1 ✕ PROD_2 ✕

PROD_3 ✕ PROD_4 ✕

Select Chains:

All Chains: ☐

Selected Delimiter: ;

Query Description: Group Mapping for PMS migration - enter the PMS cutover date in the End_Dt tab

Query Set:

```
select * from Group_Master where End_DT > @End_dt
```

Query Parameters:

size = 1

End_dt(Date) Enter Cut Off Date


- Similarly the data for the future reservations is to be extracted in this step by running the query “PMS Migration – Reservation

Check". This excel sheet will be given an appropriate name and saved on the required path.

- ICS team must confirm the following in the G3 for the current Integration
- Active Blocks
- Total reservations
- Take the screenshots of the room configuration & market segments, attach the same to the task.
- Once this is confirmed the ICS team should attach the necessary files and update the task status as complete.

Task 6.2 – Configure/Confirm Agent User under Chain Check

- ICS team should confirm and configure the agent user under the chain.
- For the same the team will go to G3 RMS –> Configuration –>Users

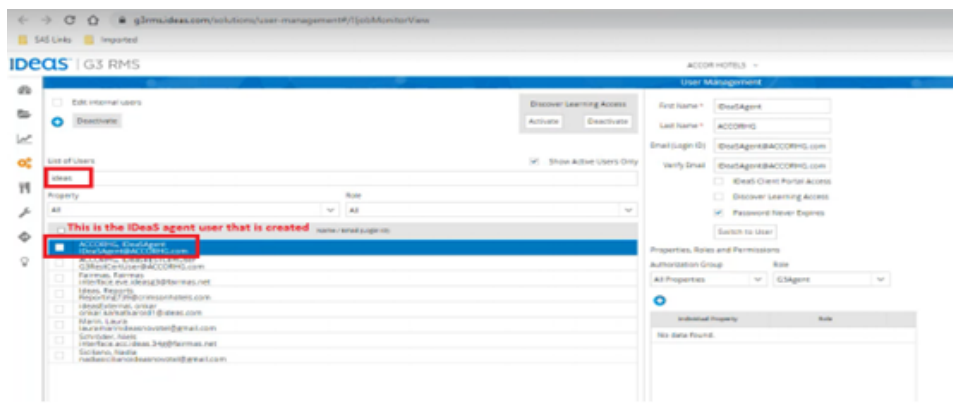


- Once this is done the task status can be marked as completed.

Note – If the agent user is not present then the team will have to co-ordinate with the QA team to add the same.

Task 7 – Set Property to Trigger Migration

- In this task the ICS team should add the property under migration screen.
- For the same go to G3 RMS –>Installation Screen –> PMS Migration Tab –>Enter the property details

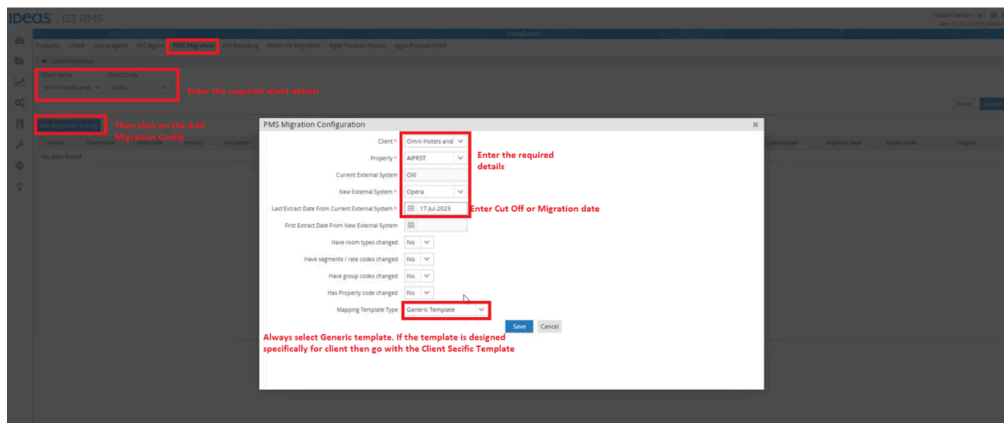

- After this the team should update the last extract date from current external system.
- Once this is done the migration parameter should be enabled.

Parameter name – pacman.feature.PMSMigrationEnabled=True

- After all the above steps are completed successfully the task status should be marked as completed.

Task 8 – Peer Review

- This task is performed by the respective migration project lead.
- The review will be done for the following
- Property Configuration
- Property Details under the migration screen
- Last update migration date
- Migration Parameter status
- Once the peer review is complete the task status is updated to complete & this will also mark the completion of Phase 1

Task 9 – Monitor Orchestrator Job

- Before starting with this task, the status of G3 application should be checked.
- After the status of application is verified, the team should monitor the orchestrator job in the G3 RMS, review the alerts

Note: The orchestrator job is monitored on the migration date.

Detailed View

- The updates should be sent to the Case Owner.
- The property gets auto moved to “dormant mode” in this stage of migration.
- Once the above steps are completed the task status should be marked as completed.
- Once the orchestrator job is complete the property will move to ‘Data Capture Mode’

Note – Check with CSS team and have the BDE triggered manually using postman application if there is a connection issue between NGI & G3.

Task 10 – Configure Property & Action Migration Alerts

- The team will have to resolve the alerts if any
- In this step the integration configuration is setup in G3
- The following information is updated
- External System
- `core.property.externalSystem.subSystem`
- Resort Code
- Past Days
- Group Past Days

- Check if the agent user is created
- Once these are done the task status is marked as completed.

Task 11 – Install Agent

- Install the agent & establish the PMS connection

Note – Confirm the connection establishment with the Oracle AMS team

- The Agent Id is received from G3 RMS->Installation -> Opera Agent ->Select the required client name

Note – Always use the Agent on which the property count is on the lower end.

- Once the agent is installed & the PMS connection is established successfully this task can be marked as completed. The same is received from the Oracle team

Task 12 – Extract Creation

- For Extract Creation the team will go to G3 RMS –> Installation –> Opera Agent –> Select the required client name –> Go to the required Agent ID –> Click on Actions –> Select the required property –> Click on Request Feeds
- In this step set the past days & group past days as per migration cutoff date.
- Once this is completed set the property to “Data Capture” mode.
- On successful completion of this step mark the task status as completed.

Task 13 – Extract Validation

- The following URL is hit to download the extract

<https://g3rms.ideas.com/pacmanplatformsecurity/rest/dataTransfer/downloadData?propertyId=990854&correlationId=6530ef26-3710-42b7-b6a2-94f903f94e52>

Note –

- Update the Property Id & the correlation ID based on the property for which the extract is to be downloaded.
- The extract will have 11 files (ct, csat, ctat, pt, psat, ptat, gb, gm, trans, yc, metadata)

- In this step verify the following
- PT file for non-zero data
- Past data & group past data
- Reservation Count
- Data received in the extract should contain the following
- Capacity
- Solds
- Revenue
- Transaction Count
- Blocks
- Room Types
- Market Segments
- Rate Codes
- Once the extract is successfully validated & the data is as expected then the task can be marked as complete.

Note – If there is production or cache issue check with QA team if the configuration parameter name cache can be cleared, post migrating the property to new system.

Task 14 – Review Active Groups received & In House and Future Reservations

- In this step check the following
- Reservation count in old & new PMS
- Old group & new group data
- Attach the necessary files and the task can be marked as completed.

Note – Refer Task 6.1

Task 15 – System Catch Up

- For the same go to the G3 RMS –>Installation –>Enter the Property Details –>Actions –> Data Mapping

- Perform the system (data extract) catch-up & confirm if it is done successfully

- Once the above step is successfully completed, manually set the property in the “Decision Creation” mode.
- Once this is done, catch up the RSS extract & monitor if it is done. For the same go to Jenkins –> G3 support-RSS extracts-catchup –> Fill in the required details

- As the property is moved manually into “Decision Creation” mode we have to run the sync so that the data can be processed. The sync that needs to be done is as follows

pacman.core.property.sync.syncRequiredForecastGroupsConfigurationChanged
pacman.core.property.sync.syncRequiredAccommodationConfigurationChanged
pacman.core.property.sync.syncRequiredSpecialEventsChanged

- In this step you must verify catch up is done for data extracts & the RSS from the cut-off date.
- Once all the necessary steps are successfully completed in this task, the task can be marked as completed.

Note – PMS Reservations are cleaned up in this step & are populated with the freshly extracted reservation details.

Task 16 – AMS Changes

- ICS team must refresh the AMS screen in the G3
- Once this is done, share this information with the case owner.
- Case Owner will further inform the client to complete the AMS
- Once the confirmation is received from the case owner & the client then the task can be marked as complete.

Note: When the AMS screen is refreshed and if there are new MS or RT that are unassigned then the client will have to complete the CCFG else Task 17 can be skipped.

Task 17 – Client to Complete CCFG

- In this step the client will complete the CCFG & review and confirm the same.
- Once the FG’s are confirmed client will have to commit the same.
- Once this is done and the CPM has informed the ICS team the task status can be marked as completed.

Task 18 – Data Verification & Decision Review and Alert Action

- In this step the client will review the data, forecast & decision review.
- There should be a confirmation received from CPM and client.
- Action alert is generated in the UI.
- Once this is received, we will update the task status to the completed.

Task 19 – Post Data Collection_Data Verification_ Decision Review

- In this step the team will take the back up of post-data
- For the same follow the Task 2 & 3 activities mentioned in [Process Document_Pre-Post Forecast & Decision Verification_1.00](#)

Task 20 – Decision Upload Confirmation

- In this step the case owner will reconfirm the first upload, post the migration to new PMS.
- Here the full upload is required and hence the case owner will create a new task that includes the format of the decisions.
- Once it is confirmed and the required steps are followed this task can be marked as completed.

Task 21 – Review Outbound

- In this step the ICS team should review the outbound and make the necessary changes wherever required.

TARS: BAR by rate code, MinLOS restriction Opera: Overbooking restriction

- This task can be then marked as completed.

Task 22 – Peer Review

- The project lead will do the review & setup the property in the required decision mode.
- This marks the completion of this task.

Task 23 – Upload Decision & Send Confirmation

- In this step the ICS team will upload the decisions & send the confirmation to the client.
- Case owner & client will send the revert confirmation for the same.
- Once all the confirmations are received the task is good to close.

Task 24 – Action Pending Migration Alerts if any

- Here the ICS team will verify if there are any pending migration alerts that require attention.

- If there are any alerts that require attention, then the team will take necessary steps and mark this step as completed.

Task 25 – Monitor G3 RMS Processing & Decision Upload

- ICS team will monitor the job for the defined number of days as mentioned in the task.
- If there are unwanted exceptions that occur during the monitoring step, then the further necessary actions can be taken to resolve the exceptions.
- If there are no exceptions that occur during the monitoring phase, then this task can be marked as completed.

7 Exit Criteria

- Migration successfully completed.
- Completion of migration project informed to the respective stakeholders and the same is confirmed by client.



0

Tagged on: agent Agent to Agent G3 Agent to Agent migration

Sneha Nirgude

21/09/2023

G3 Procedures, G3 Processes, G3 Solutions, Migrations, Processes

No Comments

← OperaFeedValidationStep Failed

Process Document_G3 Data Feed Migration to EDF →

Leave a Reply

Your email address will not be published. Required fields are marked *

Comment *

Name *

Email *

Website

☐ Save my name, email, and website in this browser for the next time I comment.

Post Comment
