



# CARE Knowledge Base

Knowledge Engine for CARE, by CARE!

## Search by Category

All categories

▼

Search

Enter a search term, select a category and click **Search** or select an icon below.

[All Articles](#)   [G2](#)   [G3](#)   [Car Park RMS](#)   [RevPlan](#)   [SmartSpace](#)   [Casper](#)   [Optix](#)   [Assets](#)

## G3 HTNG to HTNG

### Document Control

| Document Information |                                       |      |                |
|----------------------|---------------------------------------|------|----------------|
| Name of Document     | Process Document_G3 HTNG to HTNG_1.00 | -    | -              |
| Version Number       | 1.00                                  | -    | -              |
| Prepared By          | Sr. Process Analyst                   | Name | Sneha Nirgude  |
| Reviewed By          | Migration Project Lead                | Name | Hussain Mannur |
| Approved By          | Process Team Lead                     | Name | Karl Lobo      |

### Categories

Select Category

### Recent Posts

- [HLTN/hiltonEnableSmallGroupProductsAndInventoryLimitForNewPropertyStep](#)
- [Service Recovery Procedure – IDeaSOperaAgent Service in “Stopping” State](#)
- [Processing Failures Due to Data Type Mismatch for MGM Resorts](#)
- [Dynamic Optimization](#)
- [HLTN/Handling Error for SAS Dataset Encoding Job](#)

## 1 Introduction

## 1.1 Purpose

The purpose of this document is to prepare a standard process for G3 HTNG-to-HTNG migrations to ensure the timely migration of the projects and identify the different tasks performed in the migration.

## 1.2 Scope

This document will help in identifying the different steps involved in the migration of properties from G3 HTNG to HTNG, and the different teams involved in the process of migration.

## 1.3 Intended Audience

The target audience for this document is the team and the stakeholders involved in G3 HTNG-to-HTNG migration projects.  
E.g. – Project Manager, Project Lead, Team Members etc.

## 1.4 Abbreviation

| Abbreviation | Description                           |
|--------------|---------------------------------------|
| ICS          | Installation, Configuration & Support |
| ROA          | <u>Revenue Optimization</u> Analyst   |
| SPM          | Systems Performance Monitoring        |
| CPM          | Client Project Manager                |
| PID          | Property Inbound Data                 |
| SOW          | Scope of Work                         |
| RT           | <u>Room Type</u>                      |
| MS           | Market Segment                        |
| PMS          | Property Management System            |
| FVR          | <u>Forecast Validation</u> Report     |
| AMS          | Analytical Market Segment             |
| CCFG         | Create & Commit <u>Forecast Group</u> |
| RSS          | <u>Rate Shopping</u> System           |
| CMA          | Configuration Management Access       |
| BDE/DE       | Business Day End/Day End              |
| HTNG         | Hospitality Technology Next Gen       |
| NGI          | Next Gen Integration                  |

## Recent Comments

- Pranav Thakar on [Hilton/Processing Failure – non positive offset value for Product](#)
- Ranjit on [Hilton/Processing Failure – non positive offset value for Product](#)
- Ranjit on [Service Recovery Procedure – IDeaSOperaAgent Service in “Stopping” State](#)
- Ranjit on [Processing Failures Due to Data Type Mismatch for MGM Resorts](#)
- Ranjit on [Accor Client Handling Process Guide](#)

## 2 Assumptions

Estimation is based on Estimation History document.

## 3 Entry Criteria

- Project is at Initiation & Execution Stage

## 4 Pre-Requisites & Assumptions

- It is assumed that the project team has the access to the following tools & has the required knowledge to use the tools and execute the project
- G3 CMA
- G3 RMS
- NGI

## 5 Activities Performed

### Task 1 – Send & Discuss PID with the client

- In this step Case Owner will send out the PID Primary Inbound Data Switch Questionnaire and discuss the content with the client.
- The Case Owner will also familiarize themselves with supporting migration content that is available in the PMS Migration Guide

### Task 2 – Attach PID form & SOW on case level

- In this step the Case Owner will attach the filled PID form and SOW to the related case.
- Once this task is done the Case Owner will update the task with relevant comments and update the task status as completed

### Task 3- Attach HTNG Questionnaire to the case

- In this step the Case Owner will attach the filled HTNG Questionnaire to the related case.
- Once this task is done the Case Owner will update the task with relevant comments and update the task status as completed

### Task 4- Migration Date Information

- Case owner will enter the migration date into the case description along with the following details
- Cut over date
- Name and version of the new PMS
- Details of any changes in configuration moving from the old PMS to the New PMS
- Once this task is done the Case Owner will update the task with relevant comments and update the task status as completed.

### Task 5.1 – Migration Changes

- In this task the case owner will confirm the following changes  
Group Code/Group ID  
Reservation ID

Rate Codes  
Market Segment  
Room Types

- The above information (With Change or Without Change) is shared with the respective project migration team.
- Once this task is done the Case Owner will update the task with relevant comments and update the task status as completed.

Note – This is very important information that decides if a particular migration activity is with or without AMS recoding.

If the property is moving from HTNG to HTNG or OXI to HTNG – It should be ensured that the property code is changed in NGI else the data will be contaminated.

## Task 5.2 – Provide Migration Sheet to the Case Owner


- In this step the case owner will discuss the migration sheet with the client & provide the necessary mapping.
- This sheet is then shared across with the respective project migration team.

Note- This sheet will be provided if there are any migration changes. If there are no changes then the Case Owner will inform the same to the respective project migration team.

## Task 5.3 – Change Property Codes

- In this task the ICS team will setup the property under new vendor in NGI. Update general NGI config (username/password/currencies)
- Update configs specific to INV or Stat based setup
- Setup property in G3 (suspend BDE and CDP to be set to TRUE for HTNG – INV based property)
- In the case details check the PMS Integration details
- Once done go to [NGI](#) page à Search the vendor in the NGI page


Note – The vendor ID Id is case sensitive

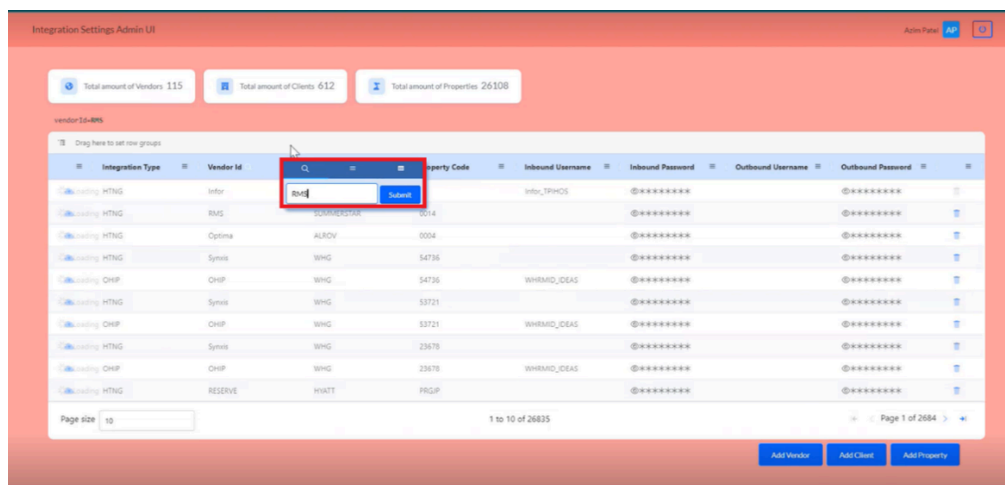

- Similarly check if the client is available there, the client should be present.

- Now check if the property is there, the property shouldn't be available here. We will now add the new property

Note – ICS will change the property code in the migration sheet to avoid any conflict in NGI. (if there is a change in property code.

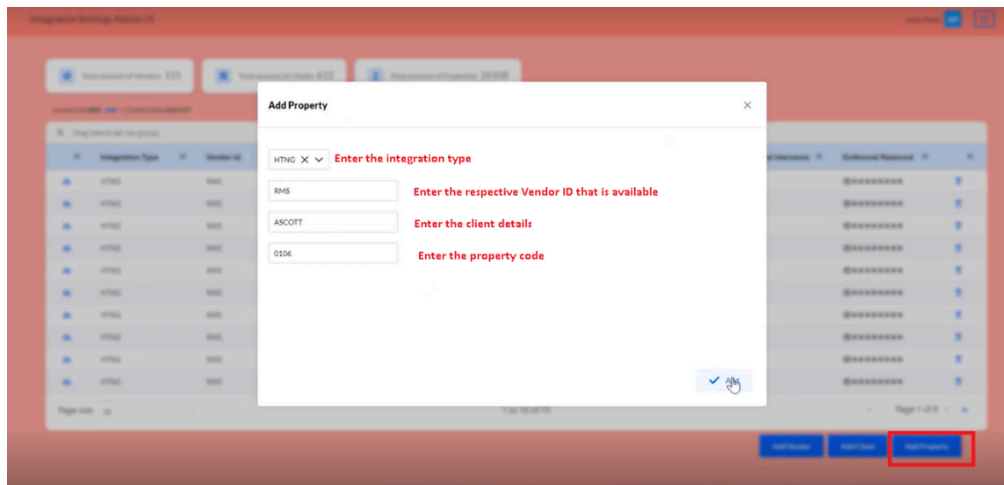

## Task 5.4 – Migration Changes Pre-data collection + C54

- In this step the team will take the back up of pre-data
- For the same follow the Task 1 activities mentioned in [Process Document\\_Pre-Post Forecast & Decision Verification\\_1.00](#)

## Task 6 – Active Block/In-House and Future Reservations Check

- Before starting this task check the status of the status of the CMA application.
- So here the ICS team will go to the [G3 CMA](#), run a query 'Group Mapping for PMS Migration' and take the dump of the group codes that is present in the existing G3 system. This excel sheet will be given an appropriate name and saved on the required path.

CONFIGURATION MANAGER

SQL Reports Admin Parameters File Explorer

Run SQL Adhoc SQL View Scheduled SQL Edit Scheduled SQL

Run SQL

Selected Query: **Group Mapping for PMS migration**

SFDC Case:  **Get**

☒ Select One or More Chains ☐ Import Property Codes

Prod Instances:

Select Chains:

All Chains: ☐

Selected Delimiter: ;

Query Description: Group Mapping for PMS migration - enter the PMS cutover date in the End\_DT tab

Query Set:

```
select * from Group_Master where End_DT > @End_dt
```

Query Parameters:

**Enter Cut Off Date**

- Similarly, the data for the future reservations will be extracted in this step by running

ing the query “PMS Migration – Reservation Check” This excel sheet will be given an appropriate name and saved on the required path.

- ICS team must confirm the following in the G3 for the current Integration Active Blocks  
Total reservations
- Take the screenshots of the room configuration & market segments, attach the same to the task.
- Once this is confirmed the ICS team should attach the necessary files and update the task status as complete.

## Task 7 – Set Property to Trigger Migration

- In this task the ICS team should add the property under migration screen.
- For the same go to G3 RMS-> Installation Screen -> PMS Migration Tab -> Enter the property details

- After this the team should update the last extract date from current external system.
- Once this is done the migration parameter should be enabled.

Parameter name – pacman.feature.PMSMigrationEnabled=True

- After all the above steps are completed successfully the task status should be marked as completed.

## Task 8 – Peer Review

- This task is performed by the respective migration project lead.
- The review will be done for the following
  - Property inbound data
  - Property Configuration
  - Property Code Change
  - Property Details under the migration screen
  - Last update migration date
  - Migration Parameter status
- Once the peer review is complete the task status is updated to complete & this will also mark the completion of Phase 1

## Task 9 – Monitor Orchestrator Job

- Before starting with this task, the status of G3 application should be checked.
- After the status of application is verified, the team should monitor the orchestrator job in the G3 RMS, review the alerts

Note: The orchestrator job is monitored on the migration date.

Detailed View

- The updates should be sent to the Case Owner.
- The property gets auto moved to “dormant mode” in this stage of migration.

- Once the above steps are completed the task status should be marked as completed.
- Once the orchestrator job is complete the property will move to 'Data Capture Mode'

Note – Check with CSS team and have the BDE triggered manually using postman application if there is a connection issue between NGI & G3.

## Task 10 – Configure Property & Action Migration Alerts

- The team will have to resolve the alerts if any
- In this step the integration configuration is setup in G3
- The following information is updated
  - External System
  - Subsystem
  - Resort Code
  - Past Days
  - Group Past Days

Note – This needs to be executed once PMS Migration Configure Inbound alert is triggered and actioned/resolved.

- 
- Once these are done the task status is marked as completed.

## Task 10a – Delete future data from Hotel\_Mkt\_Accom\_Activity table

- While migrating a property from Opera/HTNG (stat based) to OXI/HTNG (inventory based) delete future data from the hotel\_market\_accom\_activity



table using Jumpbox

Query – delete from Hotel\_Mkt\_Accom\_Activity where  
Occupancy\_DT >= 'XXXX-XX-XX' (Mention the migration date)

## Task 11 – Initiate Sync (This task will only be performed after the Peer Review)

- In this step the team will inform the HTNG vendor to initiate the sync. (If it is not done)
- Go to the case page → e-mail section → Select the sender as 'installation@ideas.com'
- From the template list select the required template. (If the template is not available for a particular PMS then select the generic template, make the required changes in the subject line, update the required information and then the mail is good to be sent.

Note – Check if the property is available on G3 & NGI.

- ICS should trigger data sync from the new PMS vendor.

Note – Ensure the sync starts from **Cutoff date** and not before that. In case there are issues – invalidate the feed/clear NGI collections and retrigger the sync

- Check the following
  - Check the Groups/RTs/MSs/Rate Codes
  - Check data counts for Transactions
  - Check Earliest **Occupancy date** received in Transactions and Inv/Summary

(should be as per cut off date)  
Check Callbacks and NACKs

Rates:

<http://us2pngiap01.ideasprod.int:9090/nucleusQualifiedRatePlans/search/findByClientCodeAndPropertyCode?clientCode=PRIME;propertyCode=1001>

<http://us2pngiap01.ideasprod.int:9090/nucleusUnqualifiedRatePlans/search/findByClientCodeAndPropertyCodeOrderByNameAsc?clientCode=PRIME;propertyCode=1001>

Group:

<http://us2pngiap01.ideasprod.int:9090/nucleusGroupBlockMasters/search/findByClientCodeAndPropertyCode?clientCode=PRIME;propertyCode=1001>

Reservation: <http://us2pngiap01.ideasprod.int:9090/nucleusReservations/criteria?search=clientCode==PRIME;propertyCode==1001&sort=createDate,DESC>  
<http://us2pngiap01.ideasprod.int:9090/nucleusReservations/criteria?search=clientCode==PRIME;propertyCode==1001&sort=earliestArrivalDate>

INV: <http://us2pngiap01.ideasprod.int:9090/nucleusInventories/criteria?search=clientCode==PRIME;propertyCode==1001&sort=lastModifiedDate,DESC>

Inventory(To check last occupancyDate) :

<http://us2pngiap01.ideasprod.int:9090/nucleusInventories/criteria?search=clientCode==PRIME;propertyCode==1001&sort=occupancyDate,ASC>

Callback:

<http://us2pngiap01.ideasprod.int:9090/htngCallbackStatuses/search/findFirstByClientCodeAndPropertyCodeAndCorrelationId?clientCode=PRIME;propertyCode=1001&correlationId=>  
<http://mn5pngiappw101.ideasprod.int:9090/htngCallbackStatuss/criteria?search=clientCode==PRIME;propertyCode==1001;successful==false&sort=createDate,DESC>

NACK: <http://us2pngiap01.ideasprod.int:9090/htngPrimaryValidations/criteria?search=clientCode==PRIME;propertyCode==1001&sort=createDate,DESC>

Ignored: <http://mn5pngiappw101.ideasprod.int:9090/htngMessageHealths/criteria?search=clientCode==PRIME;propertyCode==1001;validationStatus==IGNORED>

Rejected:

<http://mn5pngiappw101.ideasprod.int:9090/htngMessageHealths/criteria?search=clientCode==PRIME;propertyCode==1001;validationStatus==REJECTED>

Accepted:

<http://mn5pngiappw101.ideasprod.int:9090/htngMessageHealths/criteria?search=clientCode==PRIME;propertyCode==1001;validationStatus==ACCEPTED>

Valid: <http://mn5pngiappw101.ideasprod.int:9090/htngMessageHealths/criteria?search=clientCode==PRIME;propertyCode==1001;validationStatus==VALID>

Note –

- Update the Property code & the client code based on the property.

## Task 12.1 – Request Old Vendor confirmation to stop sending data to IDEaS via HTNG

- ICS team will inform the old vendor to stop sending data to IDEaS  
Note- The ICS team should receive a confirmation for the same from the vendor and then proceed to next step.

## Task 12.2 – Confirmation on Messages stopped being received in NGI

- Verify no data is received in

Note- Do not close task unless confirmed by vendor – continue follow up and continue with migration activity. Advise CPM/CRM to follow up with the client and vendor.

## Task 13 – Extract Creation

- For Extract Creation the team will go to G3 RMS ->Installation-> HTNG -> Select the required client name->Go to the required HTNG ID ->Click on Actions -> Select the required property ->Click on Request Feeds

- In this step set the past days & group past days as per migration cutoff date.
- Once this is completed set the property to “Data Capture” mode.
- On successful completion of this step mark the task status as completed.

## Task 14 – Extract Validation

- The following URL is hit to download the extract

<https://g3rms.ideas.com/pacmanplatformsecurity/rest/dataTransfer/downloadData?propertyId=990854&correlationId=6530ef26-3710-42b7-b6a2-94f903f94e52>

Note –

- Update the Property Id & the correlation ID based on the property for which the extract is to be downloaded.
- The extract will have 11 files (ct, csat, ctat, pt, psat, ptat, gb, gm, trans, yc, metadata)

- In this step verify the following  
PT file for non-zero data  
Past data & group past data  
Reservation Count  
Data received in the extract should contain the following  
Capacity  
Solds  
Revenue  
Transaction Count  
Blocks  
Room Types  
Market Segment  
Rate Codes
- Once the extract is successfully validated & the data is as expected then the task can be marked as complete.

Note – If there is production or cache issue check with QA team if the configuration parameter name cache can be cleared, post migrating the property to new system.

## Task 15 – Review Active Groups received & In House and Future Reservations

- In this step check the following  
Reservation count in old & new PMS  
Old group & new group data
- Attach the necessary files wherever necessary and the task can be marked as completed.

Note – Refer Task 6

## Task 16 – AMS Changes

- ICS team must refresh the AMS screen in the G3
- Once this is done, share this information with the case owner.
- Case Owner will further inform the client to complete the AMS
- Once the confirmation is received from the case owner & the client then the task can be marked as complete.

Note: When the AMS screen is refreshed and if there are new MS or RT that are unassigned then the client will have to complete the CCFG else Task 18 can be skipped.

## Task 17 – System Catch Up

- For the same go to the G3 RMS -> Installation -> Enter the Property Details -> Actions -> Data Mapping

- Perform the system (data extract) catch-up & confirm if it is done successfully.

- Once the above step is successfully completed, manually set the property in the “Decision Creation” mode.
- Once this is done, catch up the RSS extract & monitor if it is done. For the same go to Jenkins –>G3 support-RSS extracts-catchup–> Fill in the required details

- As the property is moved manually into “Decision Creation” mode we have to run the sync so that the data can be processed. The sync that needs to be done is as follows

pacman.core.property.sync.syncRequiredForecastGroupsConfigurationChanged  
pacman.core.property.sync.syncRequiredAccommodationConfigurationChanged  
pacman.core.property.sync.syncRequiredSpecialEventsChanged

- In this step you must verify catch up is done for data extracts & the RSS from the cut-off date.
- Once all the necessary steps are successfully completed in this task, the task can be marked as completed.

Note – PMS Reservations are cleaned up in this step & are populated with the freshly extracted reservation details.

## Task 18 – Client to Complete CCFG

- In this step the client will complete the CCFG & review and confirm the same.
- Once the FG's are confirmed client will have to commit the same.
- Once this is done and the CPM has informed the ICS team the task status can be marked as completed.

## Task 19 – Data Verification, Decision Review & Action Alert

- In this step internal review of the data, forecast & decision is done.
- Action alert is generated in the UI.
- Once this is received, we will update the task status to the completed.

## Task 20 – Decision Upload Confirmation

- In this step the case owner will reconfirm the first upload, post the migration to new PMS.
- Here the full upload is required and hence the case owner will create a new task that includes the format of the decisions.
- Once it is confirmed and the required steps are followed this task can be marked as completed.

## Task 20.1 – Post Data Collection\_Data Verification\_Decision Review

- In this step the team will take the back up of post-data
- For the same follow the Task 2 & 3 activities mentioned in [Process Document\\_Pre-Post Forecast & Decision Verification\\_1.00](#)

## Task 21- Review Outbound

- In this step the ICS team should review the outbound and make the necessary changes wherever required.

TARS: BAR by rate code, MinLOS restriction Opera: Overbooking restriction

- This task can be then marked as completed.

## Task 22 – Peer Review

- The project lead will do the review & setup the property in the 2 way mode.
- This marks the completion of this task.

## Task 23 – Upload Decision & Send Confirmation

- In this step the ICS team will upload the decisions & send the confirmation to the client.
- Case owner & client will send the revert confirmation for the same.
- Once all the confirmations are received the task is good to close.

## Task 24 – Action Pending Migration Alerts if any

- Here the ICS team will verify if there are any pending migration alerts that require attention.
- If there are any alerts that require attention, then the team will take necessary steps and mark this step as completed.

## Task 25 – Monitor G3 RMS Processing & Decision Upload

- ICS team will monitor the job for the defined number of days as mentioned in the task.
- If there are unwanted exceptions that occur during the monitoring step, then the further necessary actions can be taken to resolve the exceptions.
- If there are no exceptions that occur during the monitoring phase, then this task can be marked as completed.

## Task 26 – Delete property code from NGI Vendor Config

- ICS team should remove the old HTNG configuration from NGI
- Close task 12.2

Note – Confirm no messages are received in NGI from old HTNG

## Task 27 – SPM Monitoring

- ICS team should inform the SPM to monitor the properties under special care for defined number of days.

## 6 Exit Criteria

- Migration successfully completed.
- Completion of migration project informed to the respective stakeholders and the same is confirmed by client.



0

Tagged on: G3 HTNG to HTNG HTNG migration

Sneha Nirgude 22/09/2023

G3 Procedures, G3 Processes, G3 Solutions, Migrations, Procedures, Processes

No Comments

[← Process Document\\_G3 Data Feed Migration to EDF](#)

[CMA RESTART →](#)

## Leave a Reply

Your email address will not be published. Required fields are marked \*

Comment \*

Name \*

Email \*

Website



☐ Save my name, email, and website in this browser for the next time I comment.

Post Comment
