



CARE Knowledge Base

Knowledge Engine for CARE, by CARE!

Search by Category

All categories

▼

Search

Enter a search term, select a category and click **Search** or select an icon below.

[All Articles](#) [G2](#) [G3](#) [Car Park RMS](#) [RevPlan](#) [SmartSpace](#) [Casper](#) [Optix](#) [Assets](#)

OXI to Agent Migration

Document Control

Document Information			
Name of Document	Process Document_OXI-to-Agent_1.00	-	-
Version Number	1.00	-	-
Prepared By	Sr. Process Analyst	Name	Sneha Nirgude
Reviewed By	Migration Project Lead	Name	Nihar Joshi
Approved By	Process Team Lead	Name	Karl Lobo

Categories

Select Category

Recent Posts

- [HLTN/hiltonEnableSmallGroupProductsAndInventoryLimitForNewPropertyStep](#)
- [Service Recovery Procedure – IDeaSOperaAgent Service in “Stopping” State](#)
- [Processing Failures Due to Data Type Mismatch for MGM Resorts](#)
- [Dynamic Optimization](#)
- [HLTN/Handling Error for SAS Dataset Encoding Job](#)

1 Introduction

1.1 Purpose

The purpose of this document is to prepare a standard process for OXI-to-Agent migrations to ensure the timely migration of the projects and identify the different tasks performed in the migration.

1.2 Scope

This document should help in identifying the different steps involved in the migration of properties from OXI-to-Agent, and the different teams involved in the process of migration.

1.3 Intended Audience

The target audience for this document is the team and the stakeholders involved in OXI-to-Agent migration projects.
E.g. – Project Manager, Project Lead, Team Members etc.

1.4 Abbreviation

Abbreviation	Description
ICS	Installation, Configuration & Support
ROA	<u>Revenue Optimization</u> Analyst
SPM	Systems Performance Monitoring
CPM	Client Project Manager
PID	Property Inbound Data
SOW	Scope of Work
RT	<u>Room Type</u>
MS	Market Segment
PMS	Property Management System
FVR	<u>Forecast Validation</u> Report
AMS	Analytical Market Segment
CCFG	Create & Commit <u>Forecast Group</u>
RSS	<u>Rate Shopping</u> System
CMA	Configuration Management Access
BDE/DE	Business Day End/Day End

2 Assumptions

Estimation is based on Estimation History document.

3 Phases

This section should give the breakdown of tasks in a phase wise manner.

Phases	Tasks
1	Task 1 to Task 8

Recent Comments

- Pranav Thakar on [Hilton/Processing Failure – non positive offset value for Product](#)
- Ranjit on [Hilton/Processing Failure – non positive offset value for Product](#)
- Ranjit on [Service Recovery Procedure – IDeaSOperaAgent Service in “Stopping” State](#)
- Ranjit on [Processing Failures Due to Data Type Mismatch for MGM Resorts](#)
- Ranjit on [Accor Client Handling Process Guide](#)

2	Task 9 to Task 19
3	Task 20 to Task 25

4 Entry Criteria

- Project is at Initiation & Execution Stage

5 Pre-Requisites & Assumptions

- It is assumed that the project team has the access to the following tools & has the required knowledge to use the tools and execute the project
- G3 CMA
- G3 RMS

6 Activities Performed

Task 1 – Send & Discuss PID with the client

- In this step Case Owner should send out the PID Primary Inbound Data Switch Questionnaire and discuss the content with the client.
- The Case Owner should also familiarize themselves with supporting migration content that is available in the PMS Migration Guide

Task 2 – Attach PID form & SOW on case level

- In this step the Case Owner should attach the filled PID form and SOW to the related case.
- Once this task is done the Case Owner should update the task with relevant comments and update the task status as completed

Task 3- Attach Opera Agent Questionnaire to the case

- In this step the Case Owner should attach the filled Opera Agent Questionnaire to the related case.
- Once this task is done the Case Owner should update the task with relevant comments and update the task status as completed

Task 4- Migration Date Information

- Case owner should enter the migration date into the case description along with the following details
- Cut over date
- Name and version of the new PMS
- Details of any changes in configuration moving from the old PMS to the New PMS
- Once this task is done the Case Owner should update the task with relevant comments and update the task status as completed.

Task 5.1 – Migration Changes

- In this task the case owner should confirm the following changes
- Group Code/Group ID
- Reservation ID
- Confirmation No.
- Rate Codes
- Market Segment
- Room Types
- Property/Resort Code
- The above information (With Change or Without Change) is shared with the respective project migration team.
- Once this task is done the Case Owner should update the task with relevant comments and update the task status as completed.

Note – This is very important information that decides if a particular migration activity is with or without AMS recoding.

Task 5.2 – Provide Migration Sheet to the Case Owner

- In this step the case owner should discuss the migration sheet with the client & provide the necessary mapping.
- This sheet is then shared across with the respective project migration team.

Note- This sheet should be provided if there are any migration changes. If there are no changes then the Case Owner should inform the same to the respective project migration team.

Task 6 – Migration Changes_Pre Data Collection

- In this step the team will take the back up of pre-data
- For the same follow the Task 1 activities mentioned in [Process Document_Pre-Post Forecast & Decision Verification_1.00](#)

Task 6.1 – Active Block/In-House and Future Reservations Check

- Before starting this task check the status of the status of the CMA application.
- So here the ICS team will go to the [G3 CMA](#), run a query 'Group Mapping for PMS Migration' and take the dump of the group codes that is present in the existing G3 system. This excel sheet will be given an appropriate name and saved on the required path.
- Similarly the data for the future reservations is to be extracted in this step by running the query "PMS Migration – Reservation Check". This excel sheet will be given an appropriate name and saved on the required path.

CONFIGURATION MANAGER

SQL Reports Admin Parameters File Explorer

Run SQL Adhoc SQL View Scheduled SQL Edit Scheduled SQL

Run SQL

Selected Query: **Group Mapping for PMS migration**
 SFDC Case: **Get**

☒ Select One or More Chains ☐ Import Property Codes

Prod Instances:

PROD_1 ✕ PROD_2 ✕
 PROD_3 ✕ PROD_4 ✕

Select Chains:

All Chains: ☐

Selected Delimiter: ;

Query Description: Group Mapping for PMS migration - enter the PMS cutover date in the End_Dt tab

Query Set:


```
select * from Group_Master where End_DT > @End_dt
```

Query Parameters: size = 1
 Enter Cut Off Date

- ICS team must confirm the following in the G3 for the current Integration
- Active Blocks
- Total reservations
- Take the screenshots of the room configuration & market segments, attach the same to the task.
- Once this is confirmed the ICS team should attach the necessary files and update the task status as complete.

Task 6.2 – Configure/Confirm Agent User under Chain Check

- ICS team should confirm and configure the agent user under the chain.
- For the same the team will go to G3 RMS –>Configuration –>Users




- Once this is done the task status can be marked as completed.

Note – If the agent user is not present then the team will have to co-ordinate with the QA team to add the same.

Task 7 – Set Property to Trigger Migration

- In this task the ICS team should add the property under migration screen.
- For the same go to G3 RMS–> Installation Screen –> PMS Migration Tab –> Enter the property details

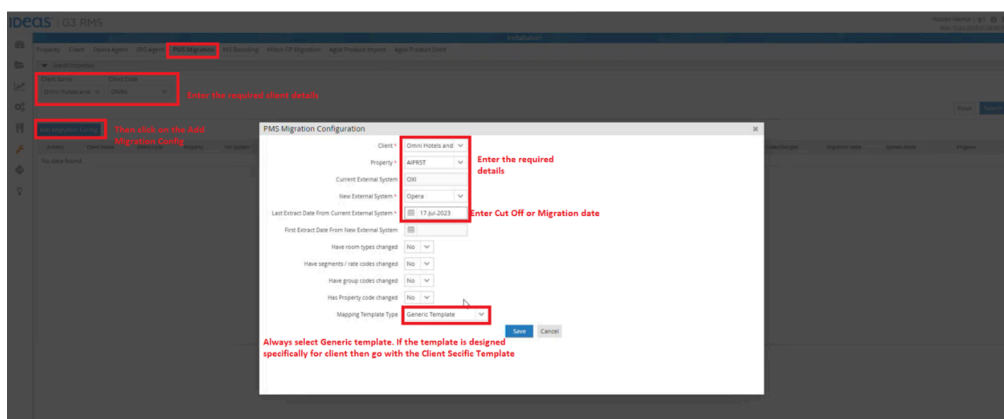

- After this the team should update the last extract date from current external system.
- Once this is done the migration parameter should be enabled.

Parameter name – pacman.feature.PMSMigrationEnabled=True

- After all the above steps are completed successfully the task status should be marked as completed.

Task 8 – Peer Review

- This task is performed by the respective migration project lead.
- The review should be done for the following
 - PID
 - Migration Screen
 - Cutoff Date
 - Agent User
- Once the peer review is complete the task status is updated to complete & this should also mark the completion of Phase 1

Task 9 – Monitor Orchestrator Job

- Before starting with this task, the status of G3 application should be checked.
- After the status of application is verified, the team should monitor the orchestrator job in the G3 RMS, review the alerts

Note: The orchestrator job is monitored on the migration date.

Detailed View

- The updates should be sent to the Case Owner.
- The property gets auto moved to “dormant mode” in this stage of migration.
- Once the above steps are completed the task status should be marked as completed.

- Once the orchestrator job is complete the property will move to 'Data Capture Mode'

Note – Check with CSS team and have the BDE triggered manually using postman application if there is a connection issue between NGI & G3.

Task 10 – Configure Property & Action Migration Alerts

- The team will have to resolve the alerts if any
- In this step the integration configuration is setup in G3
- The following information is updated
- External System
- core.property.externalSystem.subSystem
- Resort Code
- Past Days
- Group Past Days

- Check if the agent user is created
- Once these are done the task status is marked as completed.

Task 11.1 – Request Oracle confirmation to stop sending data to IDEaS via OXI

- In this step CPM/Project team should ask the Oracle team to confirm the following
- OXI processor is stopped & removed from IDEaS RMS2
- Publisher mapping & ATS removed
- Mail format –

Dear Property team,

This is to inform you that <<Property name>> has requested IDEaS RMS to be terminated w.e.f <<DATE>>

Since this was an OXI integration, please liaise with the Oracle and request them to perform the below actions:

- 1) Remove the ATS(Automatic Transmission Schedule) for inventories and blocks that were configured to be sent to us.
- 2) Remove the publisher mapping for IDEASRMS2.
- 3) Disable the OXI interface for IDEASRMS2.
- 4) Disable Business Event for IDEASRMS2.

Please confirm once the activity is completed.

In case you may have any questions please feel free to reach out to us.

Task 11.2 – Confirmation on Messages stopped being received in NGI

- In this step Project team should re-verify the following
- No data is received in NGI
- Self-confirmation of stop of data & check the stop of data with the third-party team as well.
- The same can be verified at our end using the following URL's

<http://us2pngiap01.ideasprod.int:9090/oxiMessageRates/criteria?search=clientCode==1877;propertyCode==0007;requestDateTime=gt=2022-09-19&sort=createDate,DESC>

Blocks:

<http://us2pngiap01.ideasprod.int:9090/oxiMessageAllotments/criteria?search=clientCode==1877;propertyCode==0007;requestDateTime=gt=2022-09-19&sort=createDate,DESC>

STAY :

<http://us2pngiap01.ideasprod.int:9090/oxiMessageStays/criteria?search=clientCode==1877;propertyCode==0007;requestDateTime=gt=2022-09-19&sort=createDate,DESC>

Reservations :

<http://us2pngiap01.ideasprod.int:9090/oxiMessageReservations/criteria?search=clientCode==1877;propertyCode==0007;requestDateTime=gt=2022-09-19&sort=createDate,DESC>

RTAV

<http://us2pngiap01.ideasprod.int:9090/oxiMessageRtavs/criteria?search=clientCode==1877;propertyCode==0007;requestDateTime=gt=2022-09-19&sort=createDate,DESC>

Note –

- While hitting the above URL's make the necessary changes in the Client Code, Property Code and the Request date time. (Highlighted in yellow)
- Confirm the same from vendor. This task should not be closed until the confirmation is received.

Task 12 – Install Agent

- Install the agent & establish the PMS connection

Note – Confirm the connection establishment with the Oracle AMS team

- The Agent Id is received from G3 RMS-> Installation-> Opera Agent -> Select the required client name

Note – Always use the Agent on which the property count is on the lower end.

- Once the agent is installed & the PMS connection is established successfully this task can be marked as completed. The same is received from the Oracle team

Task 13 – Confirm IdeaS seeded user is activated

- Confirm with Oracle team if the IDEaS seeded user is activated
- PMS username: IDEAS

PMS password : \$\$\$IDEAS\$\$

Note – Seeded user is the user that we use to connect the Agent to PMS. This task should not be closed until the confirmation is received.

Task 14 – Extract Creation

- For Extract Creation the team will go to G3 RMS-> Installation Opera Agent -> Select the required client name-> Go to the required Agent ID ->Click on Actions -> Select the required property -> Click on Request Feeds
- In this step set the past days & group past days as per migration cutoff date.

- Once this is completed set the property to “Data Capture” mode.
- On successful completion of this step mark the task status as completed.

Task 15 – Extract Validation

- The following URL is hit to download the extract

<https://g3rms.ideas.com/pacmanplatformsecurity/rest/dataTransfer/downloadData?propertyId=990854&correlationId=6530ef26-3710-42b7-b6a2-94f903f94e52>

Note –

- Update the Property Id & the correlation ID based on the property for which the extract is to be downloaded.
- The extract will have 11 files (ct, csat, ctat, pt, psat, ptat, gb, gm, trans, yc, metadata)

- In this step verify the following
- PT file for non-zero data
- Past data & group past data
- Reservation Count
- Data received in the extract should contain the following
- Capacity
- Solds
- Revenue
- Transaction Count
- Blocks
- Room Types
- Market Segments
- Rate Codes
- Once the extract is successfully validated & the data is as expected then the task can be marked as complete.

Note – If there is production or cache issue check with QA team if the configuration parameter name cache can be cleared, post migrating the property to new system.

Task 16 – Review Active Groups received & In House and Future Reservations

- In this step check the following
- Reservation count in old & new PMS
- Old group & new group data
- Attach the necessary files wherever necessary and the task can be marked as completed.

Note- Refer step 6.1

Task 17 – System Catch Up

- For the same go to the G3 RMS –> Installation –>Enter the Property Details –>Actions –> Data Mapping

- Perform the system (data extract) catch-up & confirm if it is done successfully

- Once the above step is successfully completed, manually set the property in the “Decision Creation” mode.
- Once this is done, catch up the RSS extract & monitor if it is done. For the same go to Jenkins –> G3 support-RSS extracts-catchup–> Fill in the required details
- As the property is moved manually into “Decision Creation” mode we have to run the sync so that the data can be processed. The sync that needs to be done is as follows

pacman.core.property.sync.syncRequiredForecastGroupsConfigurationChanged
pacman.core.property.sync.syncRequiredAccommodationConfigurationChanged
pacman.core.property.sync.syncRequiredSpecialEventsChanged

- In this step you must verify catch up is done for data extracts & the RSS from the cut-off date.

- Once all the necessary steps are successfully completed in this task, the task can be marked as completed.

Note – PMS Reservations are cleaned up in this step & are populated with the freshly extracted reservation details.

Task 18 – AMS Changes

- ICS team must refresh the AMS screen in the G3
- Once this is done, share this information with the case owner.
- Case Owner should further inform the client to complete the AMS
- Once the confirmation is received from the case owner & the client then the task can be marked as complete.

Note: When the AMS screen is refreshed and if there are new MS or RT that are unassigned then the client should have to complete the CCFG else Task 19 can be skipped.

Task 19 – Client to Complete CCFG

- In this step the client should complete the CCFG & review and confirm the same.
- Once the FG's are confirmed client should have to commit the same.
- Once this is done and the CPM has informed the ICS team the task status can be marked as completed.

Task 20 – Data Verification & Decision Review and Alert Action

- In this step the client should review the data, forecast & decision review.

- There should be a confirmation received from CPM and client.
- Action alert is generated in the UI.
- Once this is received, we should update the task status to the completed.

Task 20.1 – Post Data Collection_Data Verificaton_Decision Review

- In this step the team will take the back up of post-data
- For the same follow the Task 2 & 3 activities mentioned in [Process Document_Pre-Post Forecast & Decision Verification_1.00](#)

Task 21 – Decision Upload Confirmation

- In this step the case owner should reconfirm the first upload, post the migration to new PMS.
- Here the full upload is required and hence the case owner should create a new task that includes the format of the decisions.
- Once it is confirmed and the required steps are followed this task can be marked as completed.

Task 22 – Review Outbound

- In this step the ICS team should review the outbound and make the necessary changes wherever required.

TARS: BAR by rate code, MinLOS restriction Opera: Overbooking restriction

- This task can be then marked as completed.

Task 23 – Peer Review

- The project lead should do the review & setup the property in the 2 way mode
- This marks the completion of this task.

Task 24 – Upload Decision & Send Confirmation

- In this step the ICS team should upload the decisions & send the confirmation to the client.
- Case owner & client should send the revert confirmation for the same.
- Once all the confirmations are received the task is good to close.

Task 25 – Action Pending Migration Alerts if any

- Here the ICS team should verify if there are any pending migration alerts that require attention.
- If there are any alerts that require attention, then the team should take necessary steps and mark this step as completed.

Task 26 – Monitor G3 RMS Processing & Decision Upload

- ICS team should monitor the job for the defined number of days as mentioned in the task.
- If there are unwanted exceptions that occur during the monitoring step, then the further necessary actions can be taken to resolve the exceptions.
- If there are no exceptions that occur during the monitoring phase, then this task can be marked as completed.

Task 27 – Delete property code from NGI Vendor Config

- ICS team should remove the OXI configuration from NGI
- Close task 11.2

Note – Confirm no messages are received in NGI from OXI

Task 28 – SPM Monitoring

- ICS team should inform the SPM to monitor the properties under special care for defined number of days.

7 Exit Criteria

- Migration successfully completed.
- Completion of migration project informed to the respective stakeholders and the same is confirmed by client.



0

Tagged on: G3 OXI to Agent OXI to Agent OXI to Agent Migration

Sneha Nirgude

12/10/2023

G3 Procedures, G3 Processes, G3 Solutions, Migrations, Procedures, Processes

No Comments

← CMA RESTART

PRE-POST FORECAST & DECISION VERIFICATION →

Leave a Reply

Your email address will not be published. Required fields are marked *

Comment *

Name *

Email *

Website

☐ Save my name, email, and website in this browser for the next time I comment.

Post Comment
